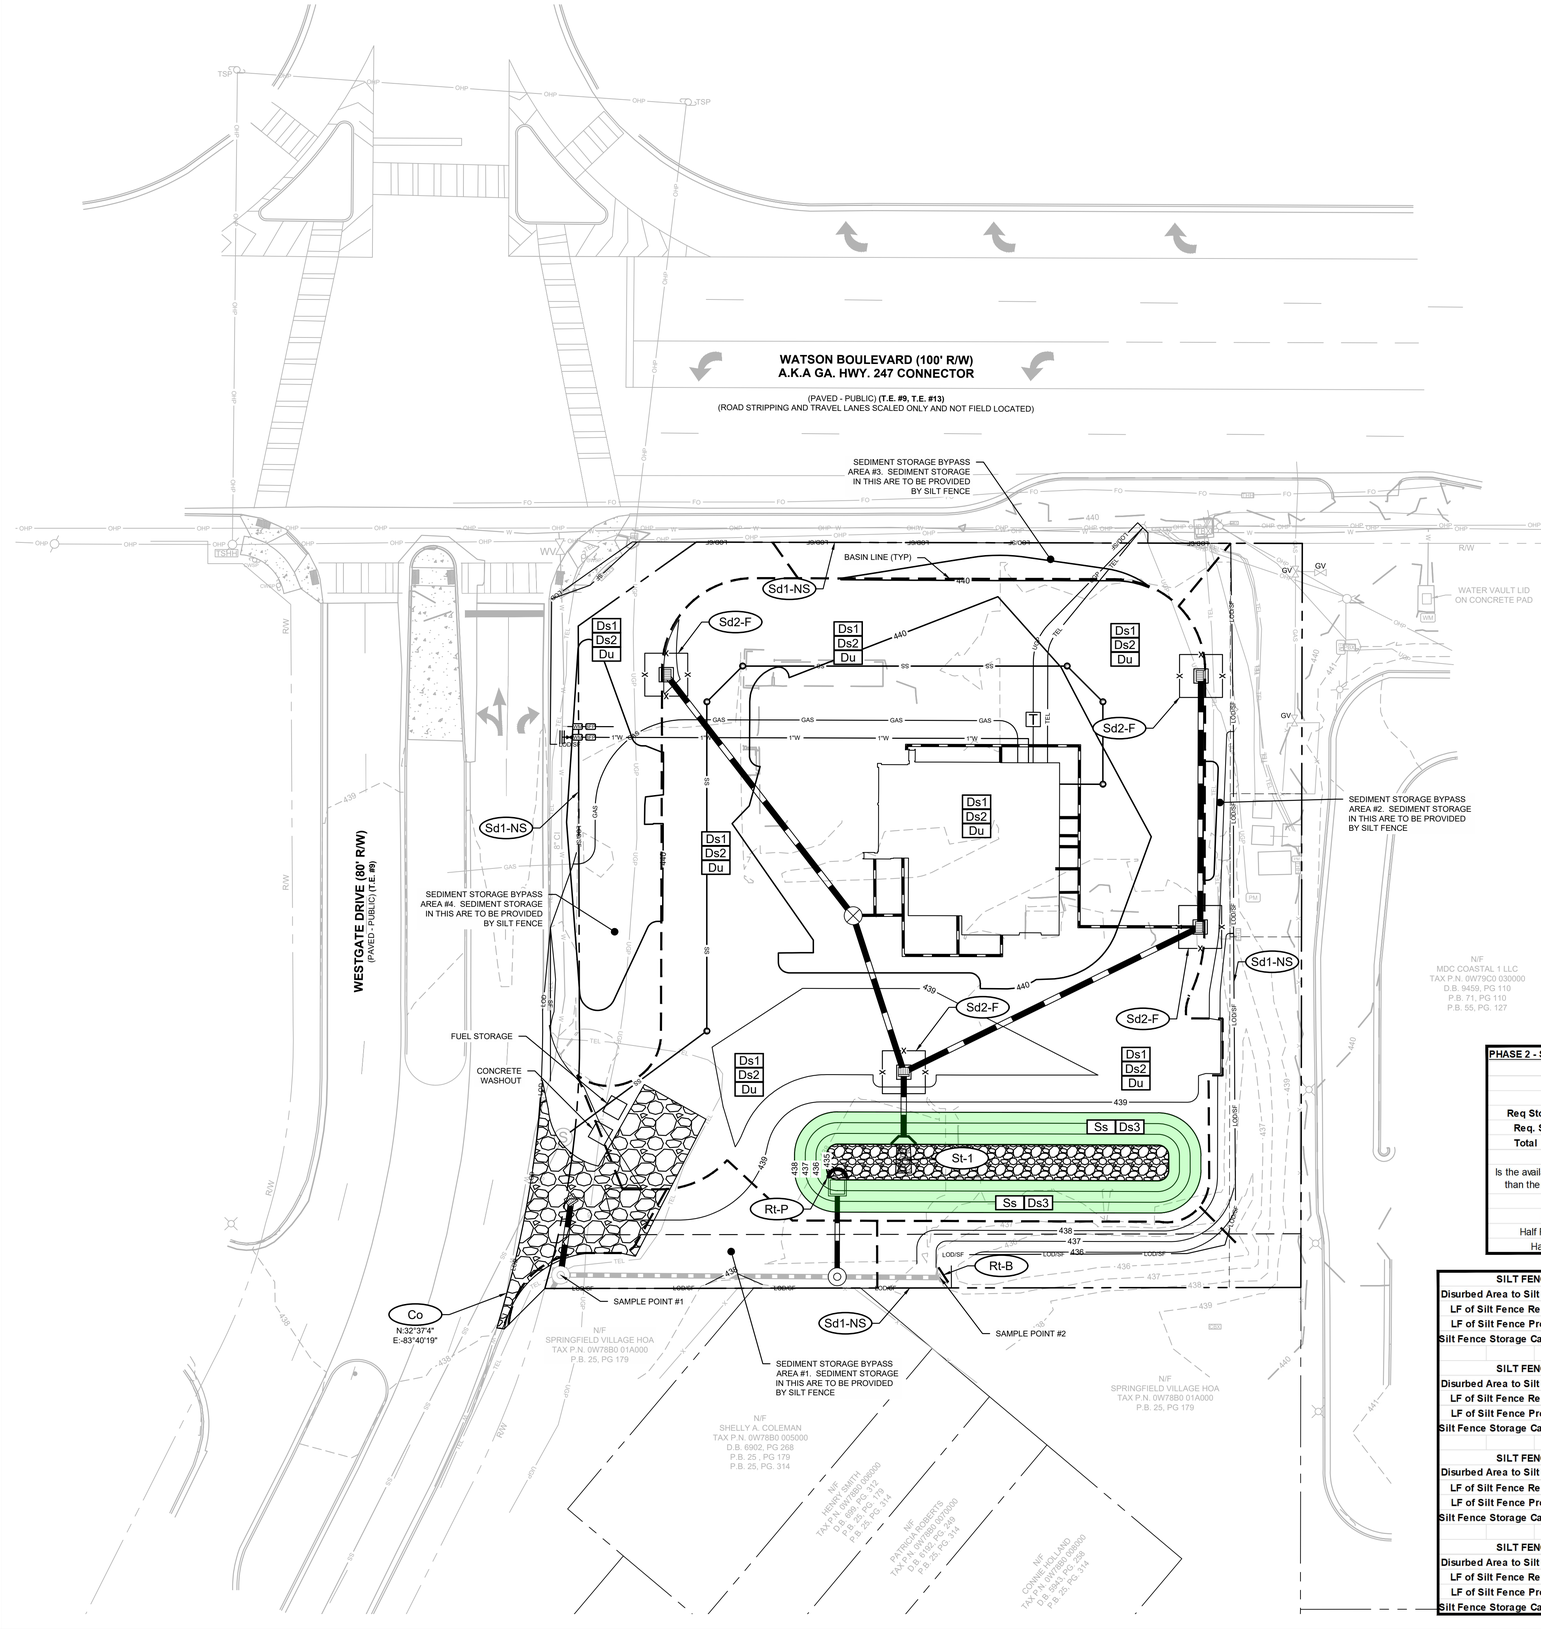


GENERAL EROSION CONTROL NOTES

3 6

1.) ALL BEST MANAGEMENT PRACTICES ARE TO BE IN ACCORDANCE WITH THE MANUAL FOR EROSION AND SEDIMENT CONTROL IN GEORGIA, PUBLISHED BY THE GEORGIA SOIL AND WATER CONSERVATION COMMISSION EROSION AND SEDIMENT CONTROL STANDARDS.
2.) BOUNDARY & TOPOGRAPHIC SURVEY BY GASKINS+LECRAW, A PAPE DAWSON COMPANY, DATED 05.08.2026. BENCHMARK IS NOTED ON SURVEY.
3.) SOIL TYPES FOR ENTIRE DISTURBED AREA IS OGA PER NRCS WEB SOIL SURVEY
4.) THE ESCAPE OF SEDIMENT FROM THE SITE SHALL BE PREVENTED BY THE INSTALLATION OF EROSION AND SEDIMENTATION CONTROL MEASURES AND PRACTICES SHALL BE INSTALLED PRIOR TO LAND DISTURBING ACTIVITIES.
5.) EROSION AND SEDIMENTATION CONTROL MEASURES AND PRACTICES SHALL BE MAINTAINED AT ALL TIMES. IF FULL IMPLEMENTATION OF THE APPROVED PLAN DOES NOT PROVIDE FOR EFFECTIVE EROSION CONTROL, ADDITIONAL EROSION AND SEDIMENT CONTROL MEASURES SHALL BE IMPLEMENTED TO CONTROL OR TREAT THE SEDIMENT SOURCE. ADDITIONAL EROSION AND SEDIMENTATION CONTROL MEASURES AND PRACTICES SHALL BE INSTALLED IF DEEMED NECESSARY BY ON-SITE INSPECTION.
6.) SEDIMENT STORAGE MAINTENANCE INDICATORS MUST BE INSTALLED IN SEDIMENT STORAGE STRUCTURES, AS REQUIRED, INDICATING THE 1/3 FULL VOLUME.
7.) MAINTENANCE OF ALL SOIL EROSION AND SEDIMENTATION CONTROL MEASURES AND PRACTICES, WHETHER TEMPORARY OR PERMANENT, SHALL BE AT ALL TIMES THE RESPONSIBILITY OF THE PROPERTY OWNER.
8.) WASHOUT OF CONCRETE DRUM AT CONSTRUCTION SITE IS PROHIBITED AND NOT ALLOWED IN WASH AREAS.

TOTAL SITE AREA = 0.96 ACRES
TOTAL DISTURBED AREA = 0.9 ACRES
PHASE 2 DISTURBED AREA = 1.0 ACRES

CERTIFICATION STATEMENT

12 13 14

I CERTIFY THAT THE PERMITTEE'S EROSION, SEDIMENTATION AND POLLUTION CONTROL PLAN PROVIDES FOR AN APPROPRIATE AND COMPREHENSIVE SYSTEM OF BEST MANAGEMENT PRACTICES REQUIRED BY THE GEORGIA WATER QUALITY CONTROL ACT AND THE DOCUMENT "MANUAL FOR EROSION AND SEDIMENT CONTROL IN GEORGIA" PUBLISHED BY THE GEORGIA SOIL AND WATER CONSERVATION COMMISSION AS OF JANUARY 1 OF THE YEAR IN WHICH LAND-DISTURBING ACTIVITY WAS PERMITTED, PROVIDES FOR THE SAMPLING OF THE RECEIVING WATER(S) OR THE SAMPLING OF STORM WATER OUTFALLS AND THAT THE DESIGNED SYSTEM OF BEST MANAGEMENT PRACTICES AND SAMPLING METHODS IS EXPECTED TO MEET THE REQUIREMENTS CONTAINED IN THE GENERAL NPDES PERMIT NO. GAR 100001."

I CERTIFY UNDER PENALTY OF THE LAW THAT THIS PLAN WAS PREPARED AFTER A SITE VISIT TO THE LOCATIONS DESCRIBED HEREIN BY MYSELF OR MY AUTHORIZED AGENT, UNDER MY SUPERVISION."

UPON THE INSTALLATION OF THE PHASE 1 EROSION CONTROL MEASURES, I WILL VISIT THE SITE TO PERFORM THE INSPECTION CERTIFICATION WITHIN 7 DAYS, ONCE NOTIFIED BY THE CONTRACTOR AND CERTIFY THE INSTALLATION OF PHASE 1 BMPS.

GEORGIA LICENSED PROFESSIONAL (SIGN) — DATE: 7/9/26

TIMOTHY KYLE SHARPE
GEORGIA LICENSED PROFESSIONAL (PRINT)

036681
GEORGIA PE#

0000065749
GEORGIA EROSION CONTROL LEVEL 2 CERTIFICATION 3

24 HOUR CONTACT

DEXTER PATTERSON
678.953.1694
FIFTH THIRD BANK
DEXTER.PATTERSON@53.COM

PRIMARY PERMITTEE

FIFTH THIRD BANK
3344 PEACHTREE ROAD 10TH FLOOR
ATLANTA, GEORGIA 30326
678.953.1694
CONTACT:
DEXTER PATTERSON

GSWCC Georgia Soil and Water Conservation Commission

2

KYLE SHARPE
Level II Certified Design Professional
CERTIFICATION NUMBER 0000065749
ISSUED: 02.17.2024 EXPIRES: 02.17.2027

NOTE

CONTRACTOR IS RESPONSIBLE FOR THE SEQUENCE AND TIMING OF ALL EROSION AND SEDIMENT CONTROL MEASURES. PHASING PLANS ARE ONLY A GENERAL GUIDE TO EROSION AND SEDIMENT CONTROL REQUIREMENTS AS DEVELOPMENT OCCURS.

PHASE 2 - SEDIMENT STORAGE TABLE

Rt-P - Retrofit with Perforated Half Round

Drainage Area	27200	SF =	0.62	AC
Req Stormwater Storage =	**1072**	**CF**		
Req. Sediment Storage =	**1130**	**CF**		(DA x 67 cy/ac x 27 cf/cy)
Total Required Storage =	**2202**	**CF**		
Available Storage =	5860	**CF**		
Is the available storage greater than the required storage?	YES			
Cleanout Elevation	436	**FT**		
Is the L:W Ratio ≥ 2:1	Yes			
Half Round CMP Diameter	2.25	**FT**		
Half Round CMP Height	2.00	FT		

SILT FENCE SEDIMENT STORAGE - PHASE 2 BYPASS # 1

Disturbed Area to Silt Fence =	1940	SF =	0.04	AC
LF of Silt Fence Required =	**18**	**LF**	(100 LF per 0.25 AC)	
LF of Silt Fence Provided =	**100**	**LF**		
Silt Fence Storage Capacity =	0.25	AC =	**452.25**	**CF**

SILT FENCE SEDIMENT STORAGE - PHASE 2 BYPASS # 2

Disturbed Area to Silt Fence =	1521	SF =	0.03	AC
LF of Silt Fence Required =	**14**	**LF**	(100 LF per 0.25 AC)	
LF of Silt Fence Provided =	**196**	**LF**		
Silt Fence Storage Capacity =	0.49	AC =	**886.41**	**CF**

SILT FENCE SEDIMENT STORAGE - PHASE 2 BYPASS # 3

Disturbed Area to Silt Fence =	1306	SF =	0.03	AC
LF of Silt Fence Required =	**12**	**LF**	(100 LF per 0.25 AC)	
LF of Silt Fence Provided =	**134**	**LF**		
Silt Fence Storage Capacity =	0.335	AC =	**606.015**	**CF**

SILT FENCE SEDIMENT STORAGE - PHASE 2 BYPASS # 4

Disturbed Area to Silt Fence =	4633	SF =	0.11	AC
LF of Silt Fence Required =	**43**	**LF**	(100 LF per 0.25 AC)	
LF of Silt Fence Provided =	**210**	**LF**		
Silt Fence Storage Capacity =	0.525	AC =	**949.725**	**CF**

EROSION CONTROL LEGEND

CODE	PRACTICE	MAP SYMBOL	CODE	PRACTICE	MAP SYMBOL
Ds1	DISTURBED AREA STABILIZATION (WITH MULCHING ONLY)	Ds1	Co	CONSTRUCTION EXIT	Co
Ds2	DISTURBED AREA STABILIZATION (WITH TEMPORARY SEEDING)	Ds2	Sd1-NS	SEDIMENT BARRIER (NON-SENSITIVE)	Sd1-NS
Du	DUST CONTROL ON DISTURBED AREAS	Du	Rt-B	SLOTTED BOARD DAM RETROFIT	Rt-B
Ds3	DISTURBED AREA STABILIZATION (WITH PERMANENT VEGETATION)	Ds3	St	STORM DRAIN OUTLET PROTECTION	St
Ss	SLOPE STABILIZATION	Ss	Rt-P	PERFORATED HALF-ROUND PIPE RETROFIT	Rt-P
Sd2-F	TEMPORARY INLET SEDIMENT TRAP (FILTER FABRIC W/ SUPPORTING FRAME)			LIMITS OF CONSTRUCTION	

PREPARED IN THE OFFICE OF:

GASKINS +LECRAW a PAPE-DAWSON company
© 2026 GASKINS + LECRAW
3475 CORPORATE WAY
SUITE A
DULUTH, GA 30096
PHONE - 678.546.8100
www.gaskinslecraw.com
PEF008127

8 REVISIONS:

REV.#	DATE	DRAWN BY:	CHECKED BY:

CLIENT
PRAXIS3
100 PEACHTREE STREET NW, SUITE 1450, ATLANTA, GEORGIA 30303

PROJECT
FIFTH THIRD BANK - WARNER ROBINS, GA
2711 WATSON BLVD
PARCEL ID: 0W0780-005000
WARNER ROBINS, HOUSTON COUNTY, GEORGIA

SEAL:

GEORGIA REGISTERED No. PE036681 PROFESSIONAL ENGINEER TIMOTHY KYLE SHARPE
7/9/2026

CALL BEFORE YOU DIG
811 Know what's below. Call before you dig.

SCALE & NORTH ARROW:
37
NORTH ARROW
0' 10' 20' 40'
SCALE: 1" = 20'

DESIGN INFO:

DRAWN BY:	JOA
DESIGNED BY:	MAT
REVIEWED BY:	TKS
JOB #:	75670007
8 DATE:	JULY 9, 2026

ESPC - PHASE 2

C-2.1

Drawing name: C:\Users\cklentz\Gaskins+LeCraw Dropbox\Shared Folders\Engineering\75670007 - Praxis3 - Fifth Third - Warner Robins_GA\CAD\CONSTR\75670007 - 03 - ESPC.dwg ESPC PLAN - PHASE 2 Jul 09, 2026 10:50am by: cklentz

This document, together with the concepts and designs presented herein, as an instrument of service, is intended only for the specific purpose and client for which it was prepared. Reuse of and improper reliance on this document without written authorization and adaptation by Gaskins + LeCraw, a Pape-Dawson Company shall be without liability to Gaskins + LeCraw, a Pape-Dawson Company, Copyright Gaskins + LeCraw, a Pape-Dawson Company, 2026
