COMcheck-Web™

Compliance Certificate

Project Information

Energy Code: 2015 IECC
Project Title: Fifth Third - Watson
Location: Warner Robins, Georgia
Climate Zone: 3a
Project Type: New Construction
Project No: 119957
All Electric: true
Is Renewable: false
Has Battery: false
Has Charger: false
Has Heat Pump true

Construction Site: **Owner/Agent:** **Designer/Contractor:**

Notes:

Energy Credits

Description	Credit
Enhanced Interior Lighting Controls	1.0

Credits: 1.0 Required 1.0 Proposed

Building Area

Description	Floor Area
1-Office (Office) : Nonresidential	1900

Envelope Compliance Certificate

Project Information

Energy Code: 2015 IECC
Project Title: Fifth Third - Watson
Location: Warner Robins, Georgia
Climate Zone: 3a
Project Type: New Construction
Vertical Glazing / Wall Area: 0.245

Construction Site: **Owner/Agent:** **Designer/Contractor:**

Envelope Assemblies

Assembly	Gross Area or Perimeter	Cavity R-Value	Cont. R-Value	Proposed U-Factor	Budget U-Factor
Roof:Roof, Insulation Entirely Above Deck, 3-Year-Aged Solar Reflectance Index = 0.00, Thermal Emittance = 0.76 (d), [Bldg. Use 1 - Office]	1933	---	34.00	0.029	0.039
Floor:Floor, Unheated Slab-On-Grade, [Bldg. Use 1 - Office] (c)	210	---	---	0.730	0.730
EAST					
Ext Wall:EAST WALL - BRICK, Metal Frame, 16" o.c., [Bldg. Use 1 - Office]	126	13.00	10.00	0.055	0.064
Ext Wall:EAST WALL - EIFS, Metal Frame, 16" o.c., [Bldg. Use 1 - Office]	698	13.00	11.50	0.051	0.064
Ext Wall:WEST WALL - BRICK, Metal Frame, 16" o.c., [Bldg. Use 1 - Office]	56	13.00	10.00	0.055	0.064
Ext Wall:WEST WALL - EIFS, Metal Frame, 16" o.c., [Bldg. Use 1 - Office]	770	13.00	11.50	0.051	0.064
Window:STOREFRONTS, Metal Frame with Thermal Break, Perf. Specs.: Product ID , SHGC 0.23, PF 0.31, VT 51.00, [Bldg. Use 1 - Office] (b)	356	---	---	0.390	0.460
Door:Door, Perf. Specs.: Product ID , SHGC 0.23, PF 0.31, VT 51.00, [Bldg. Use 1 - Office] (b)	48	---	---	0.770	0.770
Ext Wall:NORTH WALL - BRICK, Metal Frame, 16" o.c., [Bldg. Use 1 - Office]	107	13.00	10.00	0.055	0.064
Ext Wall:NORTH WALL - EIFS, Metal Frame, 16" o.c., [Bldg. Use 1 - Office]	782	13.00	11.50	0.051	0.064
Window:STOREFRONTS 3, Metal Frame with Thermal Break, Perf. Specs.: Product ID , SHGC 0.23, PF 0.31, VT 51.00, [Bldg. Use 1 - Office] (b)	207	---	---	0.390	0.460
SOUTH					
Ext Wall:SOUTH WALL - BRICK, Metal Frame, 16" o.c., [Bldg. Use 1 - Office]	96	13.00	10.00	0.055	0.064
Ext Wall:SOUTH WALL - EIFS, Metal Frame, 16" o.c., [Bldg. Use 1 - Office]	782	13.00	11.50	0.051	0.064
Window:STOREFRONTS 2, Metal Frame with Thermal Break, Perf. Specs.: Product ID , SHGC 0.23, PF 0.31, VT 51.00, [Bldg. Use 1 - Office] (b)	203	---	---	0.390	0.460
Door:Door 1, Perf. Specs.: Product ID , SHGC 0.23, PF 0.31, VT 51.00, [Bldg. Use 1 - Office] (b)	24	---	---	0.770	0.770

(a) Budget U-factors are used for software baseline calculations ONLY, and are not code requirements.

(b) Fenestration product performance must be certified in accordance with NFRC and requires supporting documentation.
(c) Slab-On-Grade proposed and budget U-factors shown in table are F-factors.
(d) High albedo roof requirement options: 1) 3-year aged solar reflectance >= 0.55 thermal emittance >= 0.75, 2) 3-year aged solar reflectance index >= 64.0, 3) Initial year aged solar reflectance >= 0.70 thermal emittance >= 0.75, 4) Initial year aged solar reflectance index >= 82.0.

Envelope PASSES: Design 13% better than code

Envelope Compliance Statement

Compliance Statement: The proposed envelope design represented in this document is consistent with the building plans, specifications, and other calculations submitted with this permit application. The proposed envelope systems have been designed to meet the 2015 IECC requirements in COMcheckWeb and to comply with any applicable mandatory requirements listed in the Inspection Checklist.

Name - Title **Signature** **Date**

Inspection Checklist

Energy Code: 2015 IECC

Requirements: 0% were addressed directly in the COM*check* software

Text in the "Comments/Assumptions" column is provided by the user in the COMcheck Requirements screen. For each requirement, the user certifies that a code requirement will be met and how that is documented, or that an exception is being claimed. Where compliance is itemized in a separate table, a reference to that table is provided.

Plan Review

Section # & Req.ID	Plan Review	Complies?	Comments/Assumptions
C103.2 [PR1]^{1}	Plans and/or specifications provide all information with which compliance can be determined for the building envelope and document where exceptions to the standard are claimed.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C402.4.2 [PR14]^{1}	In enclosed spaces > 2,500 ft2 directly under a roof with ceiling heights >15 ft. and used as an office, lobby, atrium, concourse, corridor, storage, gymnasium/exercise center, convention center, automotive service, manufacturing, non-refrigerated warehouse, retail store, distribution/sorting area, transportation, or workshop, the following requirements apply: (a) the daylight zone under skylights is >= half the floor area; (b) the skylight area to daylight zone is >= 3 percent with a skylight VT >= 0.40; or a minimum skylight effective aperture >= 1 percent.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C406 [PR9]^{1}	Plans, specifications, and/or calculations provide all information with which compliance can be determined for the additional energy efficiency package options.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C402.4.1 [PR10]^{1}	The vertical fenestration area <= 30 percent of the gross above-grade wall area.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C402.4.1 [PR11]^{1}	The skylight area <= 3 percent of the gross roof area.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	

Additional Comments/Assumptions:

1	High Impact (Tier 1)	2	Medium Impact (Tier 2)	3	Low Impact (Tier 3)

Footing / Foundation Inspection

Section # & Req.ID	Footing / Foundation Inspection	Complies?	Comments/Assumptions
C303.2 [FO4]^{2}	Slab edge insulation installed per manufacturer's instructions.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C303.2.1 [FO6]^{1}	Exterior insulation protected against damage, sunlight, moisture, wind, landscaping and equipment maintenance activities.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C104 [FO3]^{2}	Installed slab-on-grade insulation type and R-value consistent with insulation specifications reported in plans and COMcheck reports.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	*See the Envelope Assemblies table for values*
C402.2.6 [FO12]^{3}	Radiant heating systems panels insulated to >=R-3.5 on face opposite space being heated.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	*See the Envelope Assemblies table for values*

Additional Comments/Assumptions:

1	High Impact (Tier 1)	2	Medium Impact (Tier 2)	3	Low Impact (Tier 3)

Framing / Rough-In Inspection

Section # & Req.ID	Framing / Rough-In Inspection	Complies?	Comments/Assumptions
C303.1.3 [FR12]^{2}	Fenestration products rated in accordance with NFRC.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C402.5.2, C402.5.4 [FR18]^{3}	Factory-built fenestration and doors are labeled as meeting air leakage requirements.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C402.5.7 [FR17]^{3}	Vestibules are installed on all building entrances. Doors have self-closing devices.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C303.1.3 [FR13]^{1}	Fenestration products are certified as to performance labels or certificates provided.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C402.4.3 [FR10]^{1}	Vertical fenestration SHGC value.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	*See the Envelope Assemblies table for values*
C402.4.3, C402.4.3.4 [FR8]^{1}	Vertical fenestration U-Factor.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	*See the Envelope Assemblies table for values*
C402.4.4 [FR14]^{2}	U-factor of opaque doors associated with the building thermal envelope meets requirements.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	*See the Envelope Assemblies table for values*
C402.5.1.2.1 [FR19]^{1}	The building envelope contains a continuous air barrier that is sealed in an approved manner and material permeability <= 0.004 dfm/ft2. Air barrier penetrations are sealed in an approved manner.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	

Additional Comments/Assumptions:

1	High Impact (Tier 1)	2	Medium Impact (Tier 2)	3	Low Impact (Tier 3)

Mechanical Rough-In Inspection

Section # & Req.ID	Mechanical Rough-In Inspection	Complies?	Comments/Assumptions
C402.5.5, C403.2.4.3 [ME3]^{3}	Stair and elevator shaft vents have motorized dampers that automatically close.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	

Additional Comments/Assumptions:

1	High Impact (Tier 1)	2	Medium Impact (Tier 2)	3	Low Impact (Tier 3)

Insulation Inspection

Section # & Req.ID	Insulation Inspection	Complies?	Comments/Assumptions
C303.1 [IN3]^{1}	Roof insulation installed per manufacturer's instructions. Blown or poured loose-fill insulation is installed only where the roof slope is <=3 in 12.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C104 [IN8]^{2}	Installed floor insulation type and R-value consistent with insulation specifications reported in plans and COMcheck reports.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	*See the Envelope Assemblies table for values*
C402.2.6 [IN18]^{3}	Radiant panels and associated components, designed for heat transfer from the panel surfaces to the occupants or indoor space are insulated with a minimum of R-3.5.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C402.3 [IN5]^{3}	High-albedo roofs satisfy one of the following: 3-year-aged solar reflectance >= 0.55 and thermal emittance >= 0.75 or 3-year-aged solar reflectance index >= 64.0.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C104 [IN2]^{1}	Installed roof insulation type and R-value consistent with insulation specifications reported in plans and COMcheck reports. For some ceiling systems, verification may need to occur during Framing Inspection.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	*See the Envelope Assemblies table for values*
C402.5.1.1 [IN1]^{1}	All sources of air leakage in the building thermal envelope are sealed, caulked, gasketed, weather stripped or wrapped with moisture vapor-permeable wrapping material to minimize air leakage.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C303.1 [IN10]^{2}	Building envelope insulation is labeled with R-value or insulation certificate providing R-value and other relevant data.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C303.2 [IN7]^{1}	Above-grade wall insulation installed per manufacturer's instructions.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C303.2.1 [IN14]^{2}	Exterior insulation is protected from damage with a protective material. Verification for exposed foundation insulation may need to occur during Foundation Inspection.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C402.2.1 [IN17]^{3}	Insulation intended to meet the roof insulation requirements cannot be installed on top of a suspended ceiling. Mark this requirement compliant if insulation is installed accordingly.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C104 [IN6]^{1}	Installed above-grade wall insulation type and R-value consistent with insulation specifications reported in plans and COMcheck reports.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	*See the Envelope Assemblies table for values*

Additional Comments/Assumptions:

1	High Impact (Tier 1)	2	Medium Impact (Tier 2)	3	Low Impact (Tier 3)

Final Inspection

Section # & Req.ID	Final Inspection	Complies?	Comments/Assumptions
C406.4 [FI54]^{1}	Enhanced digital lighting controls efficiency package: Interior lighting has following enhanced lighting controls in accordance with Section C405.2.2: Luminaires capable of continuous dimming and being addressed individually, <= 8 luminaires controlled in combination in a daylight zone, digital control system for fixtures, "Sequence of Operations" documentation, and functional testing per Section C408.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C402.5.3 [FI51]^{3}	Where open combustion air ducts provide combustion air to open combustion fuel burning appliances, the appliances and combustion air opening are located outside the building thermal envelope or enclosed in a room, isolated from inside the thermal envelope. Such rooms are sealed and insulated.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C402.5.6 [FI37]^{1}	Weatherseals installed on all loading dock cargo doors.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	
C402.5.8 [FI26]^{3}	Recessed luminaires in thermal envelope to limit infiltration and be IC rated and labeled. Seal between interior finish and luminaire housing.	☐ Complies ☐ Does Not Comply ☐ Not Observable ☐ Not Applicable	

Additional Comments/Assumptions:

1	High Impact (Tier 1)	2	Medium Impact (Tier 2)	3	Low Impact (Tier 3)

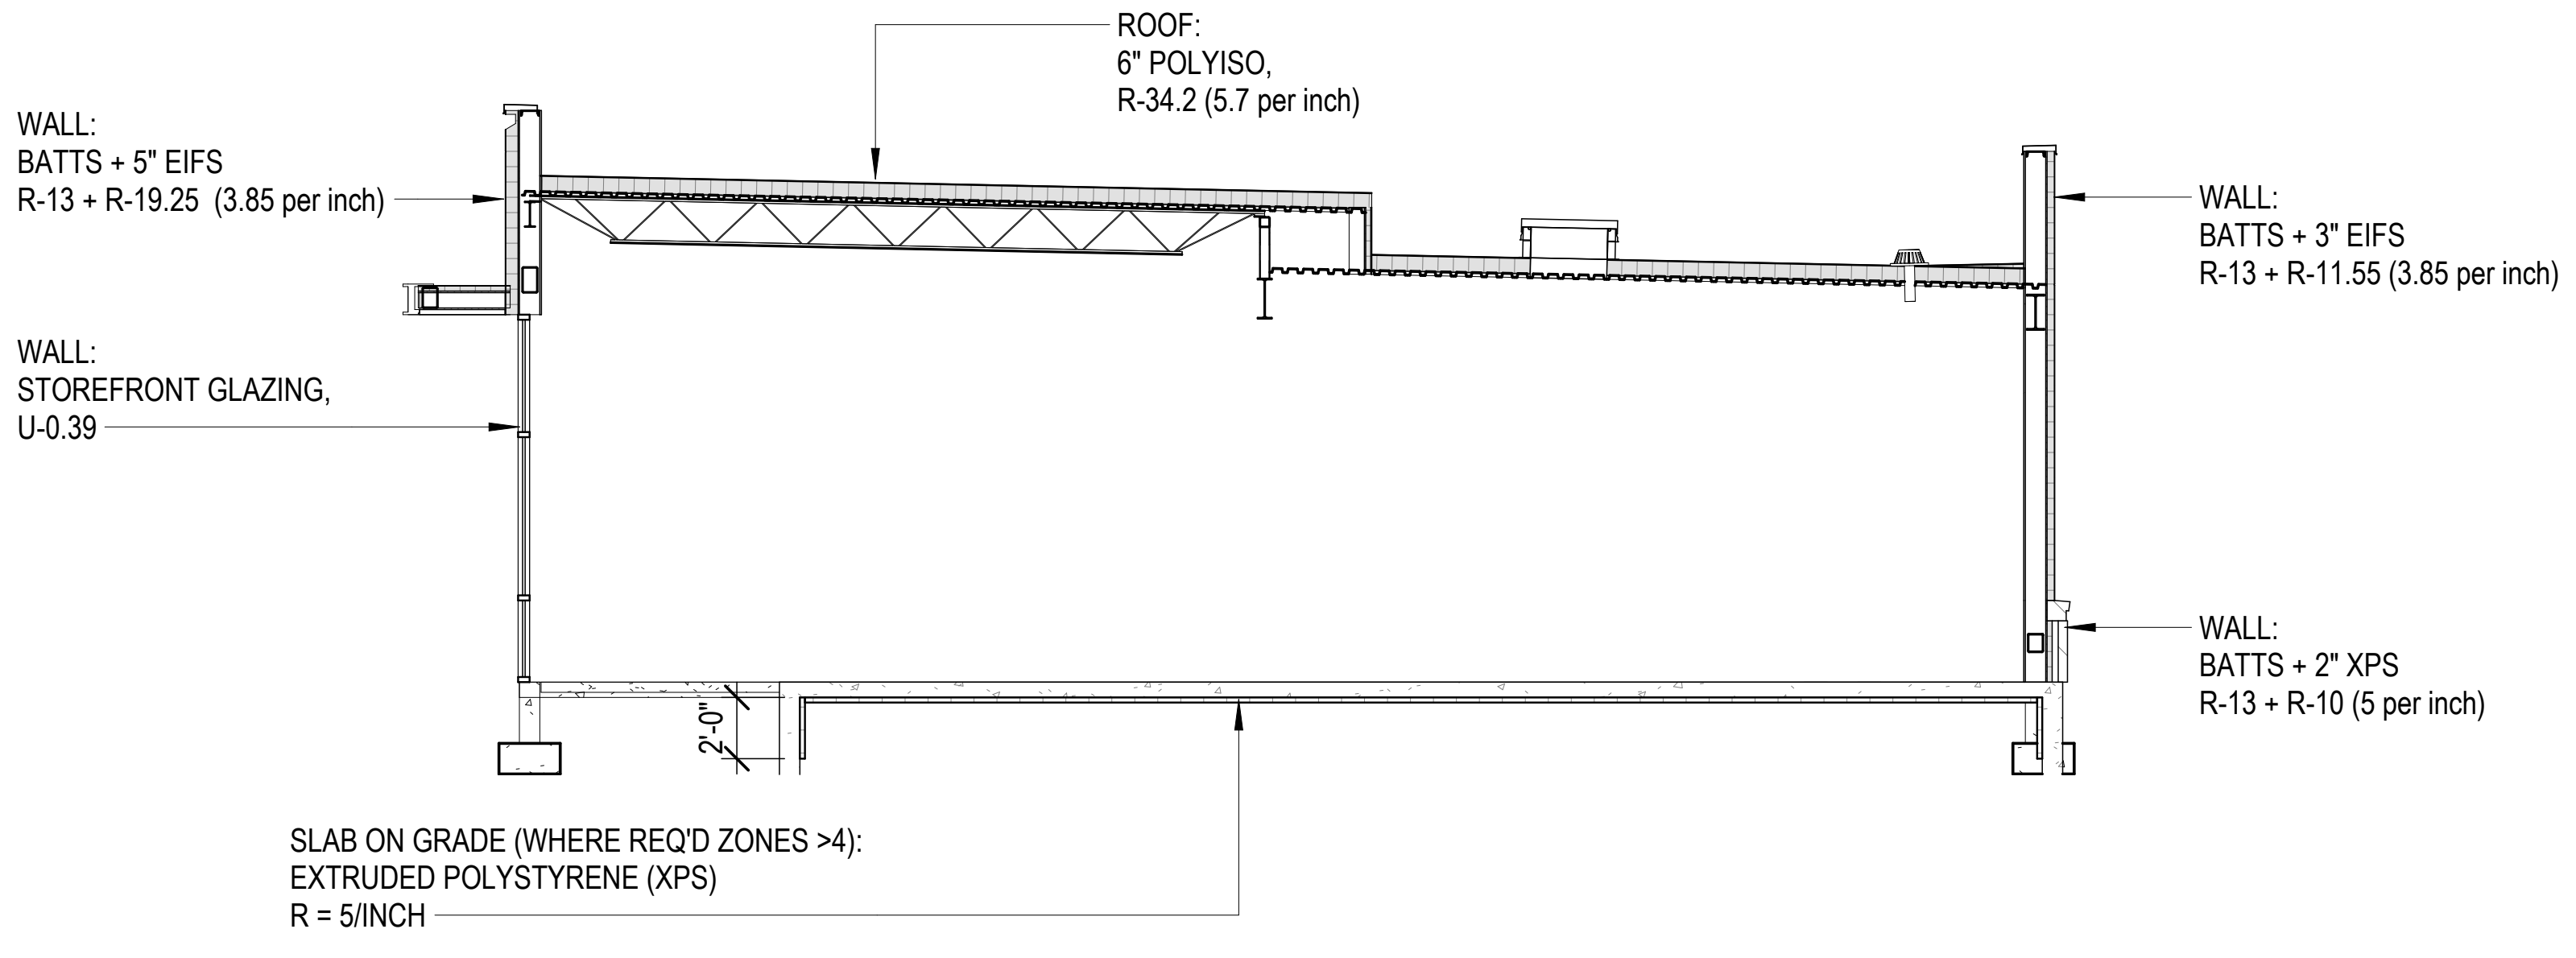

1 BUILDING ENVELOPE THERMAL VALUES
1/8" = 1'-0"

PRAXIS3

100 Peachtree St NW
Suite 1450
Atlanta, GA 30303

404-875-4500 tel
www.praxis3.com

STATE OF GEORGIA
Stuart Romm
STUART M. ROMM
07/02/26
CERTIFICATE NO. 3452
REGISTERED ARCHITECT

Copyright (c) 2026 Praxis3, LLC

All reports, plans, specifications, computer files, field data, notes and other documents and instruments prepared by Praxis3 shall retain all common law, statutory and other reserved rights, including copyright thereto.

This drawing may not be reproduced in whole or in part without written permission of Praxis3. It is to be returned upon request. Scales as stated are valid on the original drawings.

Rev	Date	Comments
	07/02/2026	PERMIT SET

Client:

FIFTH THIRD BANK

Project Number: 26302
Project Name:

WATSON BLVD.

2711 WATSON BOULEVARD
WARNER ROBINS, GA 31093

Key Plan:

Sheet Title:

COMCHECK

Sheet Number:

G-003

7/8/2026 2:37:40 PM
